Activity ID	Activity Description	Early Start	Early Finish	Orig Dur	Rem Dur	% Comp
04.01.01.26.01 Management & Integration						
M&I Management & Integration						
LK000N1120	M & I FY03	01OCT02*	30SEP03	250	250	0
LK000N1240	M & I FY04	01OCT03	30SEP04	251	251	0
LK000N1360	M & I FY05	01OCT04	30SEP05	250	250	0
LK000N1370	M & I FY06+	03OCT05	30NOV07	541	541	0
LK000N1480	Project Complete		27MAR08	0	0	0
04.01.01.26.04 Scrap Metal Removal						
1PCR Post Constr Rpt - Surge Basin, Infrast., Ditches						
LK000C5520	BJC REVIEW DRAFT D0 PCR	28MAR03	10APR03	10	10	0
LK000C5530	REVISE DRAFT D0 PCR	11APR03	02MAY03	15	15	0
LK000C5540	ISSUE D0 PCR TO DOE		02MAY03	0	0	0
LK000C5550	DOE REVIEW D0 PCR	05MAY03	03JUN03	21	21	0
LK000C5560	REVISE D0 PCR	04JUN03	17JUN03	10	10	0
LK000C5570	ISSUE D1 PCR TO DOE		17JUN03	0	0	0
LK000C5561	DOCUMENT TRANMITTAL	18JUN03	01JUL03	10	10	0
LK000C5562	ISSUE D1 PCR TO REGULATORS		01JUL03	0	0	0
LK000C5563	REGULATORS REVIEW D1 PCR	02JUL03	01AUG03	21	21	0
LK000C5564	REVISE D1 PCR	04AUG03	15AUG03	10	10	0
LK000C5565	ISSUE D2 PCR TO DOE		15AUG03	0	0	0
LK000C5566	DOCUMENT TRANSMITTAL	18AUG03	29AUG03	10	10	0
LK000C5567	ISSUE D2 PCR TO REGULATORS		29AUG03	0	0	0
LK000C5568	REGULATORS REVIEW D2 PCR	02SEP03	30SEP03	21	21	0
LK000C5580	REGULATORS APPROVE D2 PCR		30SEP03	0	0	0
2PCR Post Construction Report - Al. Ingots						
LK000C5250	DEVELOP DRAFT D0 PCR	01AUG03	14AUG03	10	10	0
LK000C5270	ISSUE DRAFT D0 PCR TO BJC		14AUG03	0	0	0
LK000C5280	BJC REVIEW DRAFT D0 PCR	15AUG03	21AUG03	5	5	0
LK000C5200	REVISE DRAFT D0 PCR	22AUG03	28AUG03	5	5	0
LK000C5300	ISSUE D0 PCR TO DOE		28AUG03	0	0	0
LK000C5305	DOE REVIEW D0 PCR	29AUG03	12SEP03	10	10	0
LK000C5310	REVISE D0 PCR	15SEP03	19SEP03	5	5	0
LK000C5210	ISSUE D1 PCR TO DOE		19SEP03	0	0	0
LK000C5311	DOCUMENT TRANSMITTAL	22SEP03	30SEP03	7	7	0
LK000C5312	ISSUE D1 PCR TO REGULATORS		30SEP03	0	0	0
LK000C5313	REGULATORS REVIEW D1 PCR	01OCT03	07OCT03	5	5	0
LK000C5314	REVISE D1 PCR	08OCT03	14OCT03	5	5	0
LK000C5315	ISSUE D2 PCR TO DOE		14OCT03	0	0	0
LK000C5316	DOCUMENT TRANSMITTAL	15OCT03	21OCT03	5	5	0
LK000C5317	ISSUE D2 PCR TO REGULATORS		21OCT03	0	0	0

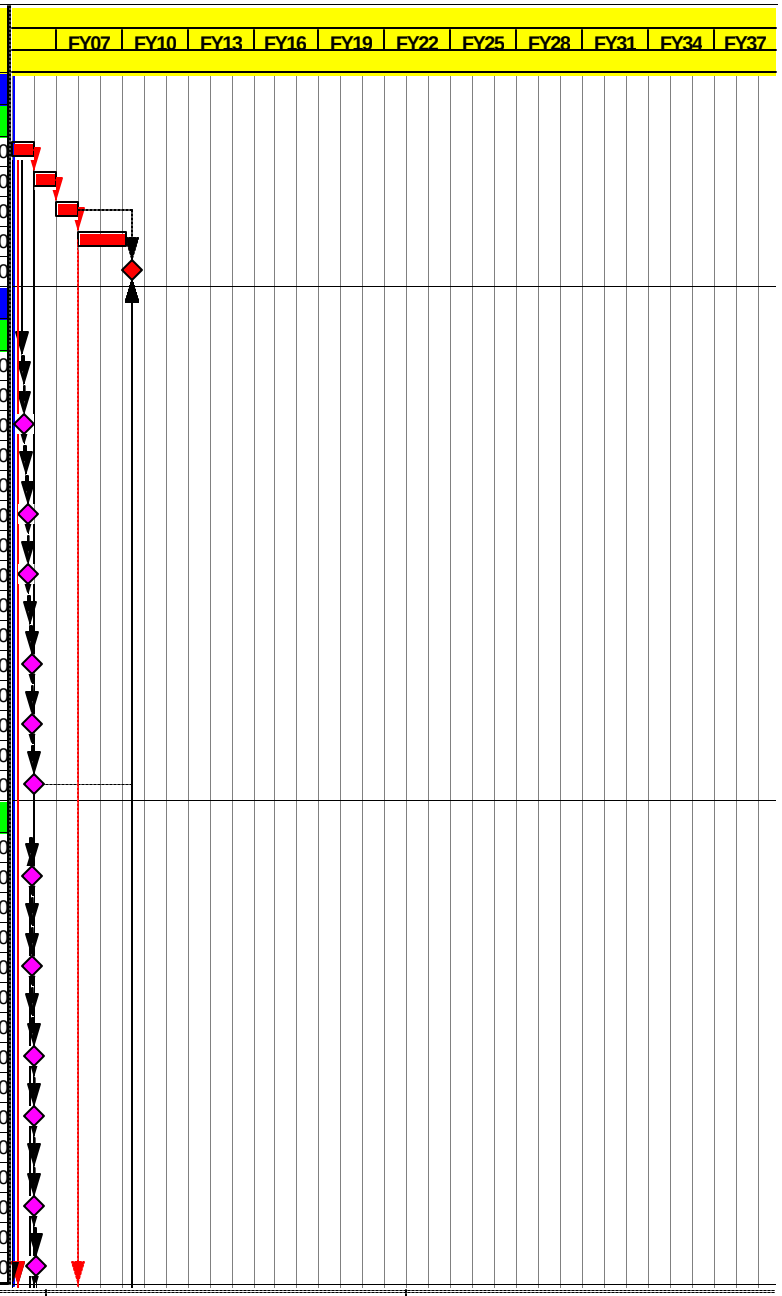

Start Date	01OCT02
Finish Date	27MAR08
Data Date	01OCT02
Run Date	09JAN04 13:21

Early Bar
Progress Bar
Critical Activity

03CT - LKCT

Sheet 1 of 7

Bechtel Jacobs Co LLC

PAD Scrap Metal Removal

Classic Schedule Layout

© Primavera Systems, Inc.

BECHTEL JACOBS
Bechtel Jacobs Company LLC

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur	Rem Dur	% Comp
LK000C5318	REGULATORS REVIEW D2 PCR	22OCT03	28OCT03	5	5	0
LK000C5290	REGULATORS APPROVE D2 PCR		28OCT03	0	0	0
3PCR Post Constr Rpt. - Nickel Ingots & Scrap Dispos						
LK000B5250	DEVELOP DRAFT D0 PCR	27NOV06	27DEC06	21	21	0
LK000B5200	ISSUE DRAFT D0 PCR TO BJC		27DEC06	0	0	0
LK000B5210	BJC REVIEW DRAFT D0 PCR	28DEC06	19JAN07	15	15	0
LK000B5230	REVISE DRAFT D0 PCR	22JAN07	02FEB07	10	10	0
LK000B5220	ISSUE D0 PCR TO DOE		02FEB07	0	0	0
LK000B5260	DOE REVIEW D0 PCR	05FEB07	05MAR07	21	21	0
LK000B5265	REVISE D0 PCR	06MAR07	19MAR07	10	10	0
LK000B5270	ISSUE D1 PCR TO DOE		19MAR07	0	0	0
LK000B5271	DOCUMENT TRANSMITTAL	20MAR07	02APR07	10	10	0
LK000B5272	ISSUE D1 PCR TO REGULATORS		02APR07	0	0	0
LK000B5273	REGULATORS REVIEW D1 PCR	03APR07	02MAY07	21	21	0
LK000B5274	REVISE D1 PCR	03MAY07	16MAY07	10	10	0
LK000B5276	SUBMIT D2 PCR TO DOE		16MAY07	0	0	0
LK000B5277	DOCUMENTAL TRANSMITTAL	17MAY07	31MAY07	10	10	0
LK0000B527	SUBMIT D2 PCR TO REGULATORS		31MAY07	0	0	0
LK000B5278	REGULATORS REVIEW D2 PCR	01JUN07	29JUN07	21	21	0
LK000B5275	REGULATORS APPROVE D2 PCR		29JUN07	0	0	0
4RAR Removal Action Report						
LK000P5295	DEVELOP DRAFT D0 REMOVAL ACTION REPORT	02JUL07	05SEP07	45	45	0
LK000P5315	ISSUE DRAFT D0 REMOVAL ACTION REPORT TO BJC		05SEP07	0	0	0
LK000P5325	BJC REVIEW DRAFT D0 REMOVAL ACTION RPT	06SEP07	04OCT07	21	21	0
LK000P5245	REVISE DRAFT D0 REMOVAL ACTION RPT	05OCT07	25OCT07	15	15	0
LK000P5335	ISSUE D0 REMOVAL ACTION REPORT TO DOE		25OCT07	0	0	0
LK000P5345	DOE REVIEW D0 REMOVAL ACTION REPORT	26OCT07	27NOV07	21	21	0
LK000P5255	REVISE D0 REMOVAL ACTION REPORT	28NOV07	11DEC07	10	10	0
LK000P5265	ISSUE D1 REMOVAL ACTION REPORT TO DOE		11DEC07	0	0	0
LK000P5256	DOCUMENT TRANSMITTAL	12DEC07	27DEC07	10	10	0
LK000P5257	ISSUE D1 REMOVAL ACTION REPORT TO REG		27DEC07	0	0	0
LK000P5258	REGULATORS REVIEW D1 REMOVAL ACTION REPORT	28DEC07	29JAN08	21	21	0
LK000P5259	REVISE D1 REMOVAL ACTION REPORT	30JAN08	12FEB08	10	10	0
LK000P5260	ISSUE D2 REMOVAL ACTION REPORT TO DOE		12FEB08	0	0	0
LK000P5261	DOCUMENT TRANSMITTAL	13FEB08	26FEB08	10	10	0
LK000P5262	ISSUE D2 REMOVAL ACTION REPORT TO REG		26FEB08	0	0	0
LK000P5263	REGULATORS REVIEW D2 REMOVAL ACTION RPT	27FEB08	27MAR08	21	21	0
LK000P5355	REG APPROVE D2 REMOVAL ACTION REPORT		27MAR08	0	0	0
ALS Aluminum Ingots						
LK000A5225	Removal of 2000 tons ingots	02JAN03	31JUL03	146	146	0
LK000A5235	Recieve manifest to acknowledge disposal appr	13JAN03	18JUN03	110	110	0
CAMP1 CAMPAIGN 1						
LKWSK01000	Campaign (2500 tons)	03JAN03	14JUL03	132*	132*	0
LKWSK01010	Evaluate for NCS Concerns	03JAN03	27MAY03	100	100	0
LKWSK01020	Shear/Torch/Crush Metal and Place in Intermodals	07JAN03	29MAY03	100	100	0
LKWSK01030	Characterize Metal for Shipment	14JAN03	05JUN03	100	100	0

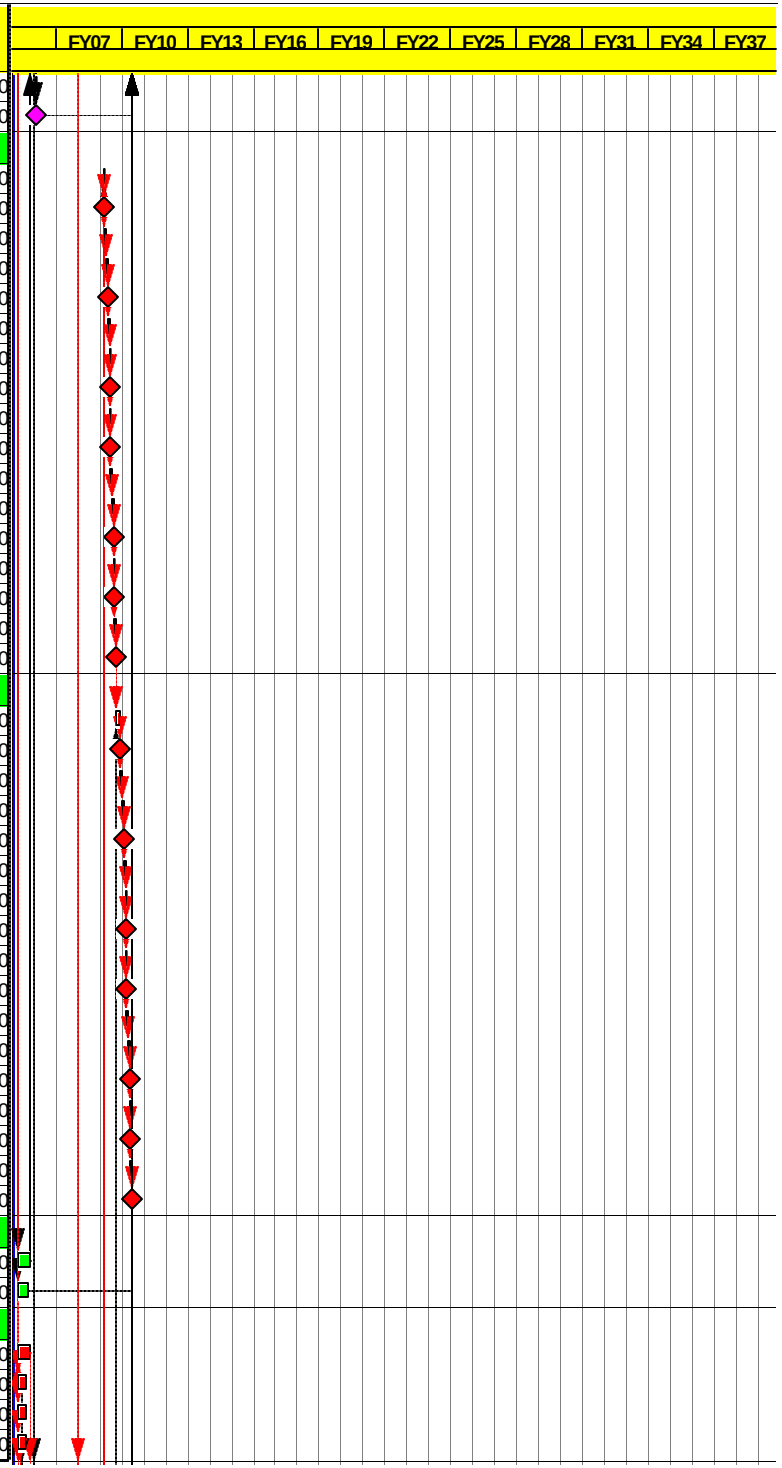

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur	Rem Dur	% Comp
LKWSK01050	Relocate container to Rail Spur	14JAN03	05JUN03	100	100	0
LKWSK01040	Produce Transportation/Disposal Manifest	12FEB03	07JUL03	100	100	0
LKWSK01060	Load Intermodal on Rail Car	19FEB03	14JUL03	100	100	0
LKWSK01061	Shipment	21FEB03	30JUL03	110	110	0
CAMP2 CAMPAIGN 2						
LKWSK01071	Campaign (1700 tons)	02JUN03	12SEP03	72*	72*	0
LKWSK01081	Evaluate for NCS Concerns	02JUN03*	29JUL03	40	40	0
LKWSK01091	Shear/Torch/Crush Metal and Place in Intermodals	04JUN03	31JUL03	40	40	0
LKWSK01101	Characterize Metal for Shipment	11JUN03	07AUG03	40	40	0
LKWSK01121	Relocate container to Rail Spur	11JUN03	07AUG03	40	40	0
LKWSK01111	Produce Transportation/Disposal Manifest	11JUL03	05SEP03	40	40	0
LKWSK01132	Load Intermodal on Rail Car	18JUL03	12SEP03	40	40	0
LKWSK01133	Shipment	22JUL03	30SEP03	50	50	0
LKWSK01070	Campaign (4100 tons)	02JAN04	30NOV04	230*	230*	0
LKWSK01080	Evaluate for NCS Concerns	02JAN04*	13OCT04	198	198	0
LKWSK01090	Shear/Torch/Crush Metal and Place in Intermodals	06JAN04	15OCT04	198	198	0
LKWSK01100	Characterize Metal for Shipment	13JAN04	22OCT04	198	198	0
LKWSK01120	Relocate container to Rail Spur	13JAN04	22OCT04	198	198	0
LKWSK01110	Produce Transportation/Disposal Manifest	11FEB04	19NOV04	198	198	0
LKWSK01130	Load Intermodal on Rail Car	18FEB04	30NOV04	198	198	0
LKWSK01131	Shipment	20FEB04	16DEC04	208	208	0
CAMP3 CAMPAIGN 3						
LKWSK01140	Campaign (12400 tons)	14OCT04	16NOV05	274*	274*	0
LKWSK01150	Evaluate for NCS Concerns	14OCT04	03OCT05	242	242	0
LKWSK01160	Shear/Torch/Crush Metal and Place in Intermodals	18OCT04	05OCT05	242	242	0
LKWSK01170	Characterize Metal for Shipment	25OCT04	12OCT05	242	242	0
LKWSK01190	Relocate container to Rail Spur	25OCT04	12OCT05	242	242	0
LKWSK01180	Produce Transportation/Disposal Manifest	22NOV04	09NOV05	242	242	0
LKWSK01200	Load Intermodal on Rail Car	01DEC04	16NOV05	242	242	0
LKWSK01201	Shipment	03DEC04	06DEC05	252	252	0
CAMP4 CAMPAIGN 4						
LKWSK01210	Campaign (4900 tons)	06OCT05	16MAY06	152*	152*	0
LKWSK01220	Evaluate for NCS Concerns	06OCT05	30MAR06	120	120	0
LKWSK01230	Shear/Torch/Crush Metal and Place in Intermodals	10OCT05	03APR06	120	120	0
LKWSK01240	Characterize Metal for Shipment	17OCT05	10APR06	120	120	0
LKWSK01260	Relocate container to Rail Spur	17OCT05	10APR06	120	120	0
LKWSK01250	Produce Transportation/Disposal Manifiest	14NOV05	09MAY06	120	120	0
LKWSK01270	Load Intermodal on Rail Car	21NOV05	16MAY06	120	120	0
LKWSK01271	Shipment	23NOV05	02JUN06	130	130	0
CAMP5 CAMPAIGN 5						
LKWSK01280	Campaign 5 (440 tons)	04APR06	21JUL06	75*	75*	0
LKWSK01290	Evaluate for NCS Concerns	04APR06	08JUN06	46	46	0
LKWSK01300	Shear/Torch/Crush Metal and Place in Intermodals	06APR06	12JUN06	46	46	0
LKWSK01310	Characterize Metal for Shipment	13APR06	19JUN06	46	46	0
LKWSK01330	Relocate container to Rail Spur	13APR06	19JUN06	46	46	0
LKWSK01320	Produce Transportation/Disposal Manifest	12MAY06	19JUL06	46	46	0

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur	Rem Dur	% Comp
LKWSK01340	Load Intermodal on Rail Car	16MAY06	21JUL06	46	46	0
LKWSK01341	Shipment	18MAY06	08AUG06	56	56	0
CAMP6 CAMPAIGN 6						
LKWSK01350	Campaign 6 (2035 tons) & (1300 tons)	13JUN06	04DEC06	120*	120*	0
LKWSK01360	Evaluate for NCS Concerns	13JUN06	18AUG06	47	47	0
LKWSK01370	Sort and Drain Shaving Drums	22JUN06	25AUG06	45	45	0
LKWSK01380	Shear/Torch/Crush Metal & Place in ROs/Piles	23JUN06	11OCT06	76	76	0
LKWSK01390	Characterize Metal	30JUN06	18OCT06	76	76	0
LKWSK01400	Relocate container from P to Rail Spur	30JUN06	18OCT06	76	76	0
LKWSK01410	Produce Transportation/Disposal Manifest	01AUG06	15NOV06	76	76	0
LKWSK01430	Develop Waste Package for P1 Yard	01AUG06	15NOV06	76	76	0
LKWSK01450	Analytical for Waste Characterization (22 tons)	02AUG06	04OCT06	45	45	0
LKWSK01460	Load Intermodal on Rail Car	08AUG06	22NOV06	76	76	0
LKWSK01470	Shipment	10AUG06	04DEC06	80	80	0
LKWSK01480	Relocate containers to Landfill from P1 yard	15AUG06	01DEC06	76	76	0
CC Contract Closeout						
LK0CCC1001	Install Gravel Pads	04DEC06	08FEB07	45	45	0
LK0CCC1002	Hyrdoseeding	09FEB07	22FEB07	10	10	0
LK0CCC1000	Complete Site Work Demobilization	23FEB07	25APR07	43	43	0
LK0CCC1010	FIELD WORK COMPLETE		25APR07	0	0	0
CM Compliance Monitoring						
LK0CCC1003	Profile Sampling	01OCT02	14OCT02	10	10	0
LKWSK01560	Sample for Anomalies FY03	01OCT02	30SEP03	250	250	0
LKWSK01570	Air monitoring Annual report FY03	01OCT02	30SEP03	250	250	0
LK0CCC1004	Analysis of Profile Sampling	15OCT02	18NOV02	25	25	0
LK0CCC1005	Develop NTS Profile and Approval	19NOV02	04FEB03	50	50	0
LKWSK01561	Sample for Anomalies	01OCT03	31MAY06	666	666	0
LKWSK01571	Air monitoring Annual report	01OCT03	31MAY06	666	666	0
GUARD Guard Rails						
LKWSK02000	Guard Rails - Design	02JAN04*	27FEB04	40	40	0
LKWSK02010	Guard Rails - Procure	01MAR04	19MAR04	15	15	0
LKWSK02020	Guard Rails - Mobilize	22MAR04	03MAY04	30	30	0
LKWSK02030	Guard Rails - Construction	04MAY04	10SEP04	90	90	0
LKWSK02031	Guard Rails - Demobilization	13SEP04	17SEP04	5	5	0
MISC Miscellaneous Activities						
LK000A0150	Operation of Basin	01OCT02	30SEP03	250	250	0
LK000A0170	Laundry	01OCT02	30SEP03	250	250	0
LK000A1080	Mobilization Cost	01OCT02*	30OCT02	22	22	0
LK000A1081	Complete Utilities on Infrastructure	01OCT02	30OCT02	22	22	0
LK000A1082	Complete Trailer Hook-up	01OCT02	30OCT02	22	22	0
LK000A1085	Seperation of Yards/Firebreak	04NOV02*	21FEB03	74	74	0
LK000A0160	Capital Equipment	30DEC02*	04AUG03	150	150	0
LK000A0230	Misc Equipment	30DEC02	04AUG03	150	150	0
LK000A1086	Storm Shelters	01MAY03*	30JUN03	42	42	0
LK000A0151	Operation of Basin	01OCT03	31MAY06	666	666	0
LK000A0171	Laundry	01OCT03	31MAY06	666	666	0

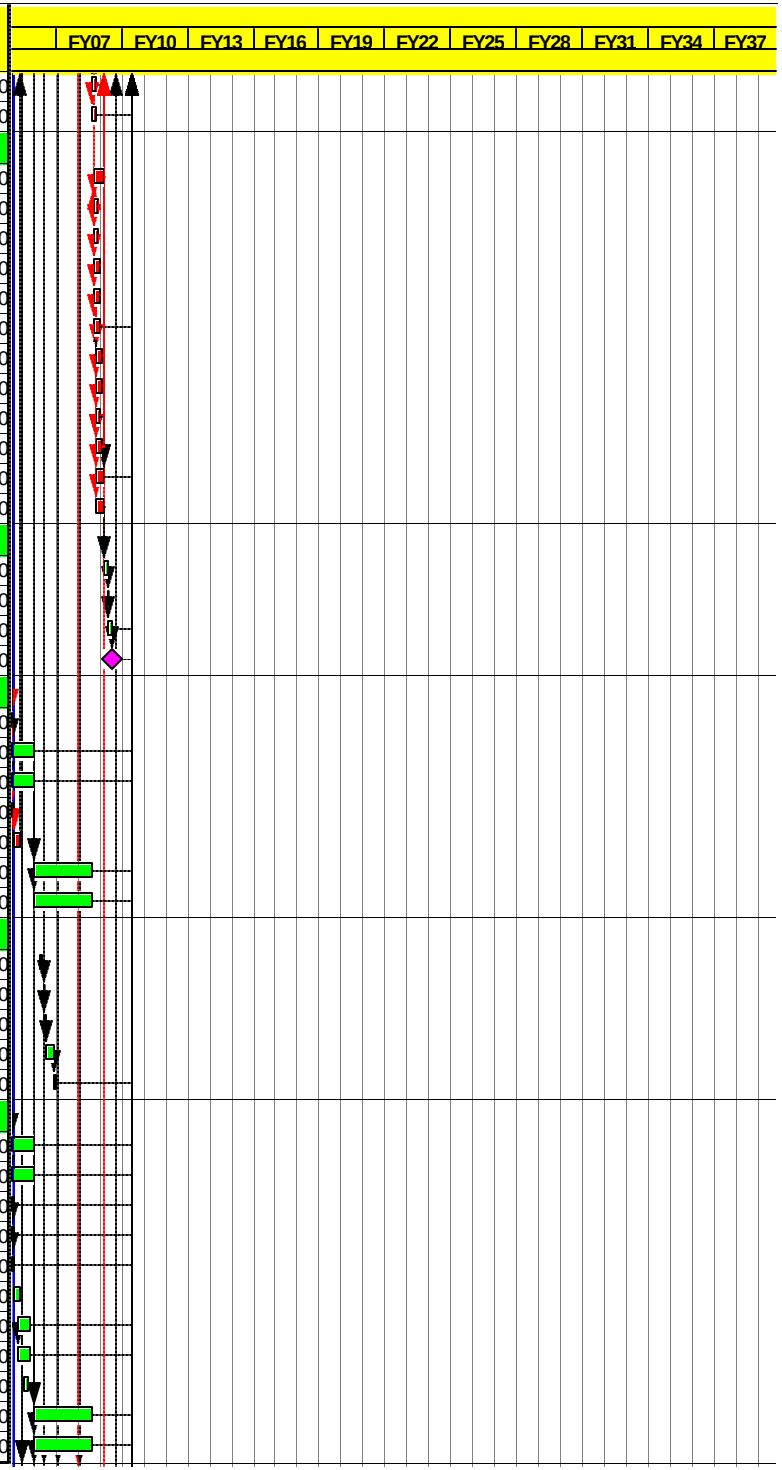

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur	Rem Dur	% Comp
LK000A0190	Training FY03	01OCT03	29SEP04	250	250	0
LK000A0200	Training FY04	30SEP04	30SEP05	251	251	0
LK000A0210	Training FY05	03OCT05	02OCT06	250	250	0
LK000A0220	Training FY06	03OCT06	31MAY07	165	165	0
NCS NCS Sampling						
LKWSK01900	OBJECT 2 (C-746-C1)	03MAR03	16MAY03	54*	54*	0
LKWSK01910	NCS Sampling - Obj 2	03MAR03	14MAR03	10	10	0
LKWSK01920	NCS Analytical - Obj 2	17MAR03	16MAY03	44	44	0
LKWSK01600	OBJECT 4 (C-746-C1)	17JUN03	03SEP03	54*	54*	0
LKWSK01610	NCS Sampling - Obj 4	17JUN03	30JUN03	10	10	0
LKWSK01620	NCS Analytical - Obj 4	01JUL03	03SEP03	44	44	0
LKWSK01700	OBJECT 5 (C-746-E1)	01MAR04	14MAY04	54*	54*	0
LKWSK01710	NCS Sampling - Obj 5	01MAR04	12MAR04	10	10	0
LKWSK01720	NCS Analytical - Obj 5	15MAR04	14MAY04	44	44	0
LKWSK01800	OBJECT 3 (C-746-E)	11NOV04	02FEB05	54*	54*	0
LKWSK01810	NCS Sampling - Obj 3	11NOV04	24NOV04	10	10	0
LKWSK01820	NCS Analytical - Obj 3	29NOV04	02FEB05	44	44	0
LKWSK01500	OBJECT 1 (C-746-C)	03NOV05	25JAN06	54*	54*	0
LKWSK01510	NCS Sampling - Obj 1	03NOV05	16NOV05	10	10	0
LKWSK01520	NCS Analytical - Obj 1	17NOV05	25JAN06	44	44	0
NICK Nickel Ingots						
LKWSK01440	C-746-H4 (11026 tons)	03OCT05	22NOV06	287*	287*	0
LKWSK01456	Pre mode Activity	03OCT05	11NOV05	30	30	0
LKWSK01462	Readiness Review	14NOV05	15NOV05	2	2	0
LKWSK01464	NTP	16NOV05		0	0	0
LKWSK01466	Foundation	16NOV05	28NOV05	7	7	0
LKWSK01472	Erect Shells	29NOV05	15DEC05	13	13	0
LKWSK01474	Finish Elect Hardware	16DEC05	28DEC05	7	7	0
LKWSK01476	As-bulits/Demob	29DEC05	10JAN06	8	8	0
LKWSK01420	Nickel Ingot Relocation	11JAN06	22NOV06	220	220	0
04.01.01.26.05 Classified Scrap Metal						
4PCR Post Constr. Rpt. for Classified Scrap						
LKAS100220	DEVELOP DRAFT D0 PCR	23MAY06	13JUN06	15	15	0
LKAS100230	ISSUE DRAFT D0 PCR TO BJC		13JUN06	0	0	0
LKAS100150	BJC REVIEW DRAFT D0 PCR	14JUN06	27JUN06	10	10	0
LKAS100160	REVISE DRAFT D0 PCR	28JUN06	20JUL06	15	15	0
LKAS100170	ISSUE D0 PCR TO DOE		20JUL06	0	0	0
LKAS100180	DOE REVIEW D0 PCR	21JUL06	18AUG06	21	21	0
LKAS100190	REVISE D0 PCR	21AUG06	01SEP06	10	10	0
LKAS100200	ISSUE D1 PCR TO DOE		01SEP06	0	0	0
LKAS100191	DOCUMENT TRANSMITTAL	05SEP06	18SEP06	10	10	0
LKAS100192	ISSUE D1 PCR TO REGULATORS		18SEP06	0	0	0
LKAS100193	REGULATORS REVIEW D1 PCR	19SEP06	17OCT06	21	21	0
LKAS100194	REVISE D1 PCR	18OCT06	31OCT06	10	10	0
LKAS100195	ISSUE D2 PCR TO DOE		31OCT06	0	0	0
LKAS100196	DOCUMENT TRANSMITTAL	01NOV06	14NOV06	10	10	0

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur	Rem Dur	% Comp
LKAS100197	ISSUE D2 PCR TO REGULATORS		14NOV06	0	0	0
LKAS100198	REGULATORS REVIEW D2 PCR	15NOV06	15DEC06	21	21	0
LKAS100210	REGULATORS APPROVE D2 PCR		15DEC06	0	0	0
CWAS Classified Scrap Metal						
LKAS100502	Develop SAP	01OCT02	09JAN03	68	68	0
LKAS100506	Develop WM Plan	01OCT02	30JUL03	207	207	0
LKAS100509	Design & construct fencing around C-746-D Task 2	01OCT02	15OCT02	11	11	0
LKAS100080	Develop Security Plan for Truck Shipment	03DEC02	23JUL03	159	159	0
LKAS100011	Characterize for shipment (pre-characterization)	10JAN03	24JAN03	10	10	0
LKAS100012	Analysis/Verification of pre-char. samples	27JAN03	11MAR03	32	32	0
LKAS100050	Develop NTS Profile	11FEB03	01AUG03	120	120	0
LKAS100515	Prepare staging area (laydown gravel) Task 1	12MAR03	15APR03	25	25	0
LKAS100501	Develop Work Packages	14JUL03	08AUG03	20	20	0
LKAS100503	Procure 120 Boxes (7.5x7.5x2)	14JUL03	29JUL03	12	12	0
LKAS100505	Procure Crane, 2 Forklifts, Scale, etc	14JUL03	13AUG03	23	23	0
LKAS100511	Design and Build Gate to D yard	14JUL03	29AUG03	35	35	0
LKAS100060	Submit Profile for NTS approval		01AUG03	0	0	0
LKAS100070	NTS Review of waste profile	04AUG03	15AUG03	10	10	0
LKAS100504	Procure Metal Shears & associated equipment	04AUG03	30SEP03	41	41	0
LKAS100517	Review work control package	11AUG03	12AUG03	2	2	0
LKAS100519	Incorporate Comments	13AUG03	13AUG03	1	1	0
LKAS100009	Receive Crane, etc.	14AUG03	18AUG03	3	3	0
LKAS100521	Review final work control packages	14AUG03	15AUG03	2	2	0
LKAS100100	Waste Profile approved by NTS		15AUG03	0	0	0
LKAS100522	Approval of work control package	15AUG03	15AUG03	1	1	0
LKAS100014	Readiness Review for Classified Scrap Metal	18AUG03	20AUG03	3	3	0
LKAS100507	Procure remaining Boxes (7.5x7.5x2)	20AUG03	05SEP03	12	12	0
LKAS100010	Mobilization of Equipment	21AUG03	22AUG03	2	2	0
LKAS100040	Process '00' sheets and load into containers	25AUG03	30SEP03	26	26	0
LKAS100518	Receive 120 boxes (7.5x7.5x2)	25AUG03	19SEP03	19	19	0
LKAS100110	Load containers on truck (ship NTS)	28AUG03	30SEP03	23	23	0
LKAS100508	Procure ST-90 boxes	08SEP03	23SEP03	12	12	0
LKAS100041	Process remaining '00' sheets & load containers	01OCT03	04DEC03	45	45	0
LKAS100111	Load containers on truck (ship NTS) FY04	01OCT03	30DEC04	312	312	0
LKAS100512	Receive Metal Shears	01OCT03	21OCT03	15	15	0
LKAS101000	Receive remaining boxes (7.5x7.5x2) (60)	01OCT03	21OCT03	15	15	0
LKAS101001	Receive ST-90 boxes	15OCT03	21MAY04	151	151	0
LKAS100042	Process '000' sheets & load containers	05DEC03	07APR04	85	85	0
LKAS100043	Process '00' & '000' shells/pallets & load boxes	08APR04	17AUG04	90	90	0
LKAS100044	Process & Load asbestos/unclassified debris	18AUG04	20OCT04	45	45	0
LKAS100090	Decon/demob heavy equipment & area deanup	21OCT04	28JAN05	66	66	0
04.01.01.26.06 DOE Prime						
DOE DOE Prime						
LKAS100124	DOE Prime for Scrap Dispos. fy03	07MAR03	30SEP03	143	143	0
LKAS100151	DOE Prime for Scrap Dispos. fy04	01OCT03	30SEP04	251	251	0
LKAS100125	DOE Prime for Classified Scrap	05MAR04	06JUN06	564	564	0

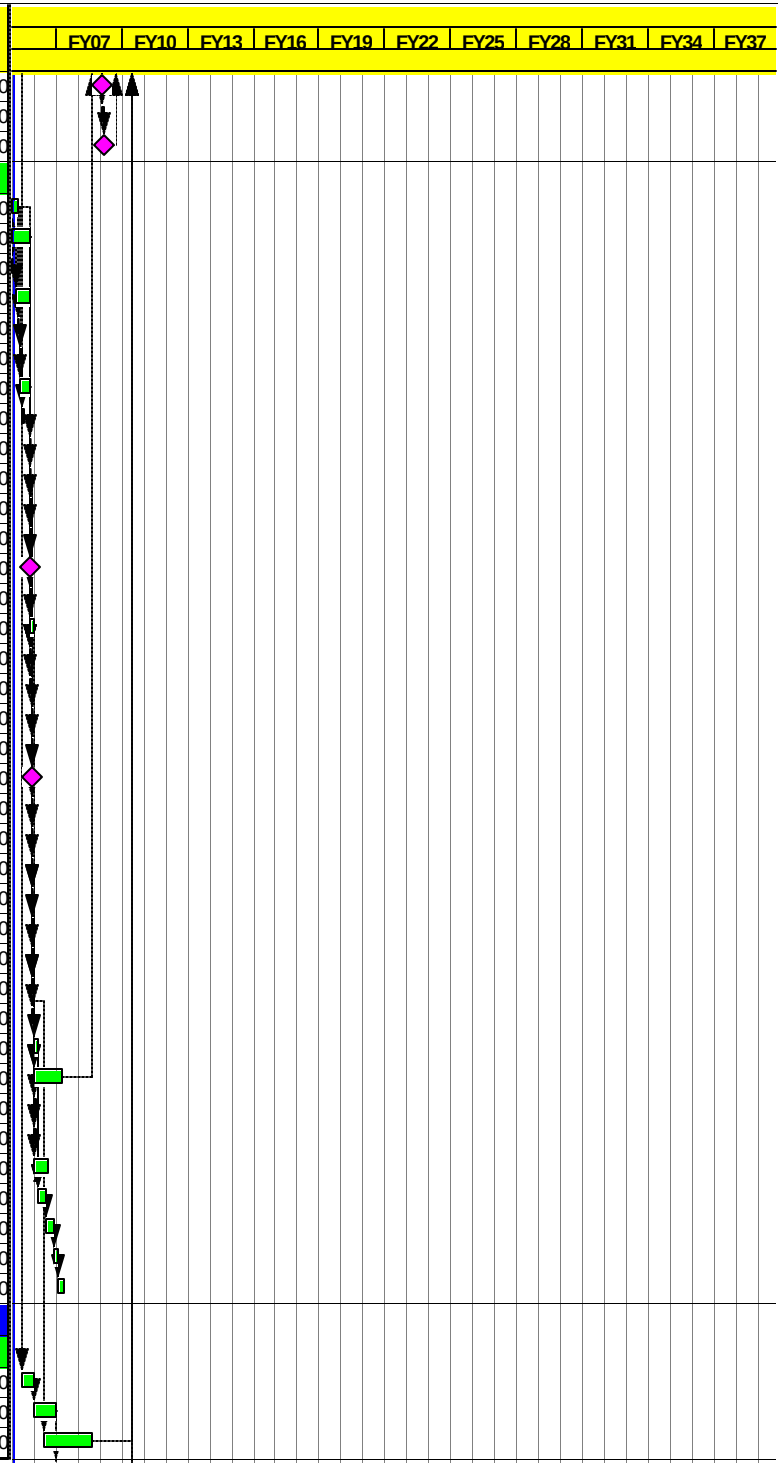

Activity ID	Activity Description	Early Start	Early Finish	Orig Dur	Rem Dur	% Comp
LKAS100121	DOE Prime for Scrap Dispos. fy05	01OCT04	30SEP05	250	250	0
LKAS100122	DOE Prime for Scrap Dispos. fy06 - Envirocare	03OCT05	30JUN06	187	187	0
LKAS100123	DOE Prime for Scrap Dispos. fy06 - NTS	03OCT05	30JUN06	187	187	0
